


# Town of Gawler Redbanks Road - Project Update



JULY 2023

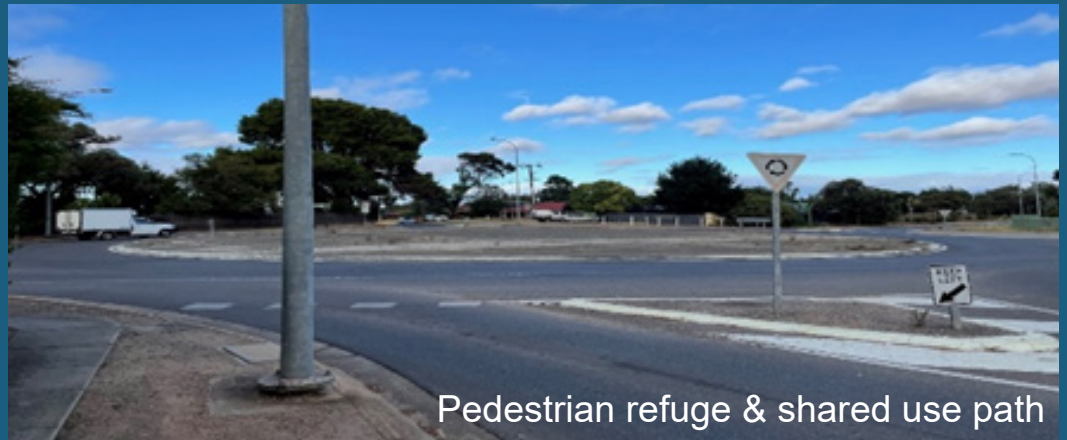

Pedestrian refuge & shared use path


Town of Gawler has been fortunate to receive funding from the South Australian Government through the Community Infrastructure Grant Program for the upgrading of pedestrian crossing points at the Redbanks Road / Weyland Road / Haines Road / Dawson Road roundabout. The project will include a new shared used path and installation of a pedestrian crossing refuge facility on Redbanks Road, north of the roundabout.

Council would like to announce Camco has been awarded the contract and will begin construction in July 2023. The project time-line is scheduled for approx. 4 months, July to October 2023 (weather permitting).

**camco** SA P L

Morgan Court will also be upgraded with new kerbing and road reconstruction. During works, it is advised to avoid the area due to the high volume of activity.

VMS boards will be displayed prior to the project commencing. Night works will be included to minimise impacts to pedestrians and road users during the construction period.

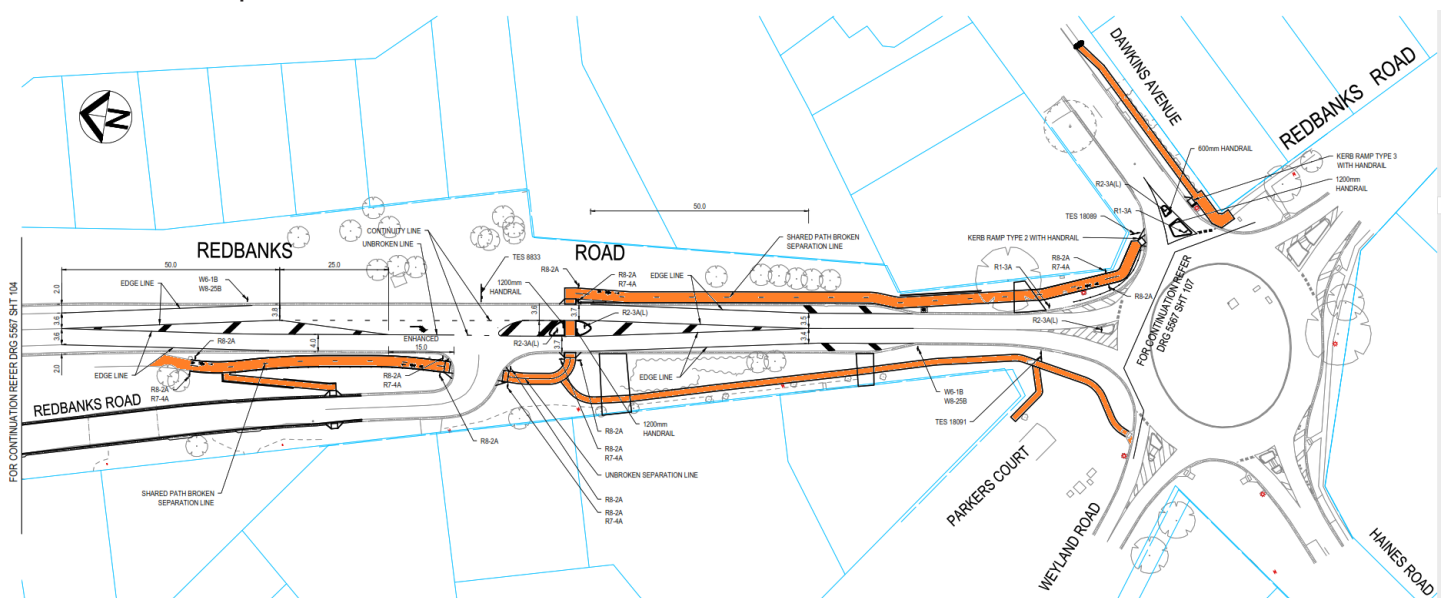

# Staging of Project

24.7.2023

<b>ESTABLISHMENT</b>	<ul style="list-style-type: none"><li>• Site establishment</li><li>• Service locations</li><li>• Survey set out</li></ul>
<b>RETAINING WALLS</b>	<ul style="list-style-type: none"><li>• Prepare, supply and commence construction of retaining walls</li></ul>

## STAGE 1 - MORGAN COURT

11.8.2023-23.8.2023

<b>CONCRETE</b>	<ul style="list-style-type: none"><li>• Excavation and base preparation</li><li>• Concrete kerbing works (kerb, inverts, spoon drain, pram ramps etc)</li><li>• Concrete footpath (Redbanks Road to Morgan Court section)</li></ul>
<b>CROSSOVERS</b>	<ul style="list-style-type: none"><li>• Excavation and base preparation</li><li>• 30mm AC7 driveway crossovers</li></ul>
<b>MISCELLANEOUS</b>	<ul style="list-style-type: none"><li>• Formation of batters and swale drain</li></ul>
<b>ROAD PAVEMENT</b>	<ul style="list-style-type: none"><li>• Excavation, 150mm PM2/20 sub-base course and 180mm PM1/20 base course</li><li>• Profiling and asphalt works</li></ul>

## STAGES 2 TO 6 - REDBANKS ROAD

31.8.2023-26.9.2023

<b>ELECTRICAL / CST</b>	<ul style="list-style-type: none"><li>• CST trenching. Note road crossing to be undertaken as night works</li></ul>
<b>STAGE 2</b>	<ul style="list-style-type: none"><li>• Shared use path - excavation, base preparation and AC7 seal inc. pedestrian ramps</li><li>• Commencement of fencing works</li></ul>
<b>STAGE 3</b>	<ul style="list-style-type: none"><li>• Driveway crossovers - excavation, base preparation and AC7 seal</li><li>• Concrete footpath - excavation, base preparation and concrete works</li><li>• Drainage swale</li></ul>
<b>STAGE 4</b>	<ul style="list-style-type: none"><li>• Concrete footpath - excavation, base preparation and concrete works</li></ul>
<b>STAGE 5</b>	<ul style="list-style-type: none"><li>• Driveway crossovers - excavation, base preparation and AC7 seal</li><li>• Shared use path - excavation, base preparation and AC7 seal inc. pedestrian ramps</li><li>• Concrete footpath - excavation, base preparation and concrete works</li></ul>
<b>STAGE 6</b>	<ul style="list-style-type: none"><li>• Profiling (night works)</li><li>• Median islands (night works)</li><li>• Asphalt and line marking (night works)</li></ul>
<b>ELECTRICAL</b>	<ul style="list-style-type: none"><li>• Stobie pole erection</li></ul>

## DEMOBILISATION

21.9.2023-22.9.2023

<b>DEMOBILISATION</b>	<ul style="list-style-type: none"><li>• Clean and tidy site</li><li>• Demobilisation</li><li>• Post construction documentation</li></ul>
-----------------------	--

## Connect with Council

For more information on this project please contact the Town of Gawler on:

**Phone** 8522 9211

**Email** [council@gawler.sa.gov.au](mailto:council@gawler.sa.gov.au)
